BRHAT BANGALORE MAHANAGARA PALIKE
INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Improvements to Roadand drains at Bhuvaneshawarinagara main Road Right side in Ward No. 06 Dasarahalli Village Limit	
2	Estimate Cost	60.00 Lakhs	
3	Administrative Approved No and Date	525/13-14, Date. 23.12.2013	
4	Technical sanction No. and Date	198/2013-14, Date. 23.12.2013	
5	Job Code No. and P Code No.	006-14-000026	
6	Tender Direct Entrested to KRIDL	KRIDL	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	Not Applicable	
8	Tender Approved Details	Not Applicable	
9	Work Order No and Date	391/2013-14, Date. 21.02.2014	
10	Stipulation time of Completion	60 Days	
11	Actiual Date of Commencement	01.05.2015	
12	Actiual Date of Completion	30.05.2014	
13	Delay if any	Nil	

	Reason for Delay	Nil	
15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verfied	Enclosed	
18	Date of Inspection		
19	MB No. and Page No.	Mb 8907 Page No.190647-670	
20	BR No. and Date	106/31.05.2014	
21	Test Result	Quality Test Report submitted by Civil Tech Consultant and Engineers is verified and Enclosed	
22	Section officer	Sri K Devegowda J.E	
23	Sub Division Office	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
a	Work Quality	Satisfactory	
b	Comments	Work completed as per MB	

Executive Engineer
Byatarayanapura Division
Yalahanka Zone, B.B.M.P.
Bangalore-560092

2/7/15

Y C Kale gowda
Executive Engineer (Retd)

Improvements to Roads and Drains at Bhuvaneshwarinagara Main Road Right Side in Ward No. 06 in Dasarahalli Village Limits.

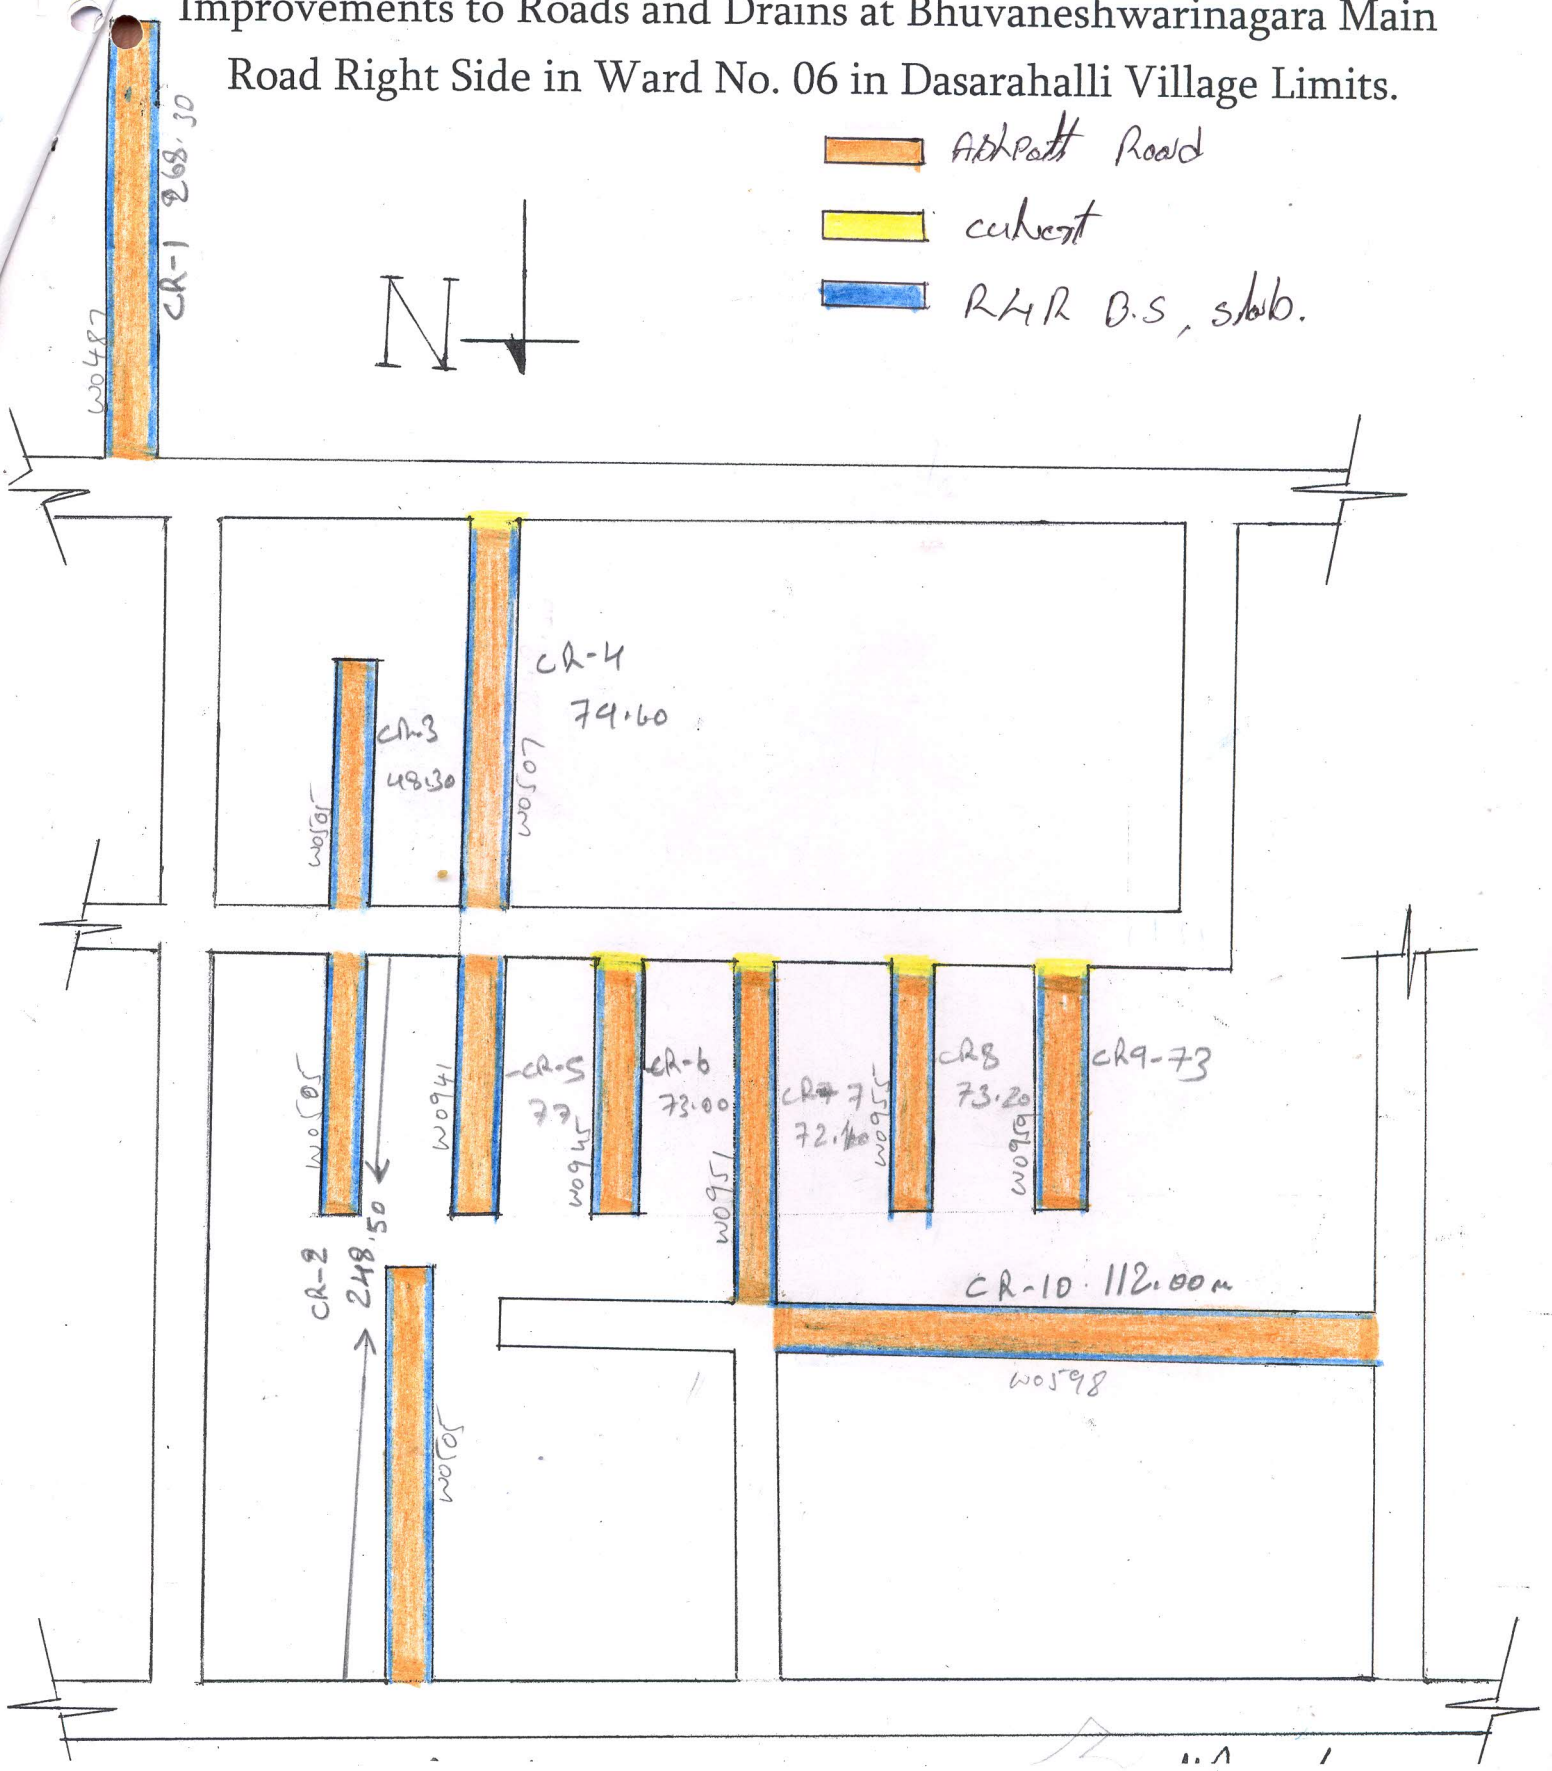

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

G.7
